OMB No. 2040-0042 Approval Expires 4/30/07

EPA

United States Environmental Protection Agency
Washington, DC 20460

PLUGGING AND ABANDONMENT PLAN

Name and Address of Facility
Resolute Natural Resources Company
1675 Broadway, Suite 1950, Denver, CO 80202

Name and Address of Owner/Operator
Resolute Aneth, LLC.
1675 Broadway, Suite 1950, Denver, CO 80202

Locate Well and Outline Unit on Section Plat - 640 Acres

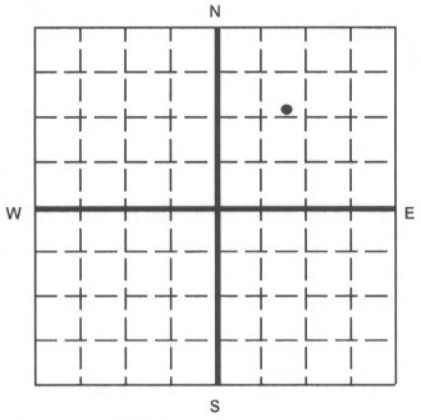

State	County	Permit Number
Utah	San Juan	

Surface Location Description
1/4 of se 1/4 of nw 1/4 of ne 1/4 of Section 13 Township 40s Range 23e

Locate well in two directions from nearest lines of quarter section and drilling unit

Surface Location 740_ ft. frm (N/S) _N__ Line of quarter section
and 1665 ft. from (E/W) E Line of quarter section.

TYPE OF AUTHORIZATION
- [x] Individual Permit
- [ ] Area Permit
- [ ] Rule

Number of Wells 1

Lease Name Aneth Unit

WELL ACTIVITY
- [ ] CLASS I
- [x] CLASS II
  - [x] Brine Disposal
  - [ ] Enhanced Recovery
  - [ ] Hydrocarbon Storage
- [ ] CLASS III

Well Number C-113 LDVL

CASING AND TUBING RECORD AFTER PLUGGING

SIZE	WT (LB/FT)	TO BE PUT IN WELL (FT)	TO BE LEFT IN WELL (FT)	HOLE SIZE
16	65	80	80	20
11.75	60	1520	1520	14.75
7.625	26.4 & 33.7	5535	5535	9.5

METHOD OF EMPLACEMENT OF CEMENT PLUGS
- [x] The Balance Method
- [ ] The Dump Bailer Method
- [ ] The Two-Plug Method
- [ ] Other

CEMENTING TO PLUG AND ABANDON DATA:	PLUG #1	PLUG #2	PLUG #3	PLUG #4	PLUG #5	PLUG #6	PLUG #7
Size of Hole or Pipe in which Plug Will Be Placed (inches)	6.5 OH	6.5 OH	6.5 OH	6.5 OH	7.625	7.625	7.625
Depth to Bottom of Tubing or Drill Pipe (ft.)	7267	7225	7183	7141	7217	5850	2130
Sacks of Cement To Be Used (each plug)	19.4	19.4	19.4	19.4	41.97	21.14	21.14
Slurry Volume To Be Pumped (cu. ft.)	23.04	23.04	23.04	23.04	49.53	24.96	24.96
Calculated Top of Plug (ft.)	7167	7125	7083	7041	7030	5750	2030
Measured Top of Plug (if tagged ft.)							
Slurry Wt. (Lb./Gal.)	15.6	15.6	15.6	15.6	15.6	15.6	15.6
Type Cement or Other Material (Class III)	A	A	A	A	A	A	A

LIST ALL OPEN HOLE AND/OR PERFORATED INTERVALS AND INTERVALS WHERE CASING WILL BE VARIED (if any)

From		To	From		To
Perfs:	7335	7470	Lat #4 OH:	7091	10765
Lat #1 OH:	7217	10963			
Lat #2 OH:	7175	10153			
Lat #3 OH:	7133	10831			

Estimated Cost to Plug Wells
$52,000 See Attachment for additonal cement plugs

Certification

I certify under the penalty of law that I have personally examined and am familiar with the information submitted in this document and all attachments and that, based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibliity of fine and imprisonment. (Ref. 40 CFR 144.32)

Name and Official Title *(Please type or print)*	Signature	Date Signed
Dwight E Mallory, Regulatory Coordinator		5/1/07

EPA Form 7520-14 (Rev. 8-01)
